


Piped water Supply in 37 peripheral villages of Talcher Coalfields

The Project was approved by MCL in August'2017. The DPR cost is 17.05 Crore. It is a deposit-based scheme where MCL deposits the fund in instalments tied with millstones to Collector Angul and the scheme is being implemented by RWSS deptt. MCL has deposited 4.44 Cr till date against which, UC of Rs. 0.55 Crore has been received.

The scheme is divided into 6 sub-packages. These are segregated into 3 packages at MCL end from fund disbursement and monitoring point of view:.

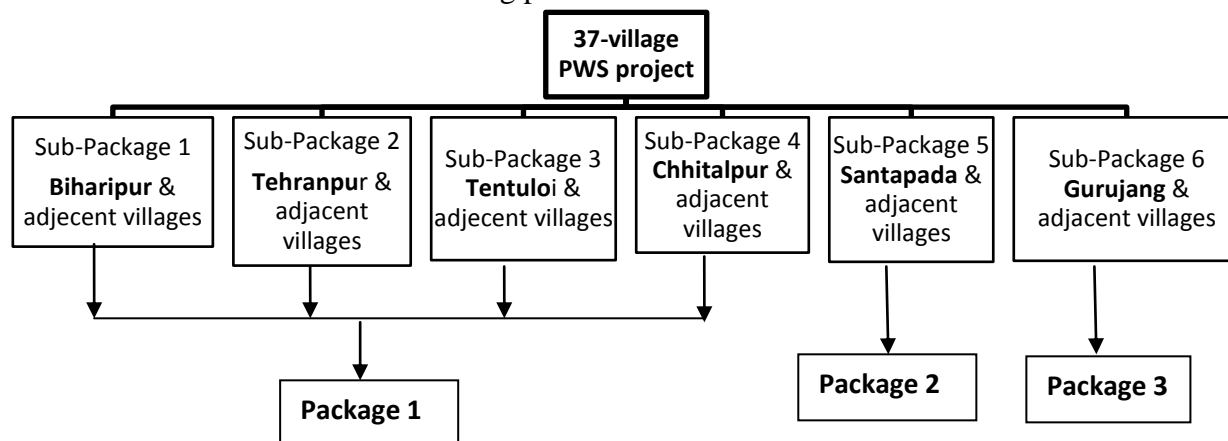

Supply matrix:

	Villages	Source	Amt	Population			Design hrs per day	Design LPCD	Features
				2011	2018 Base	2048 Designed			
1	Bihari-pur etc	Intake well Brahmani	0.58 Cr	1311	2862	4946	10	@100	100% household + 15 stand posts, Pressure filter
2	Tehran-pur etc	Open well at Jagannathpur canal	1.19 Cr	1125	3650	5840	8	@100	Pressure filters. Household distribution already exists
3	Tentuloi etc	Open well neat Tentuloi school	0.83 Cr	1761	3826	6122	8	@100	Open well to OH tank. Pr filter,
4	Chhital-pur etc	Intake well Singida river	0.80 Cr	1488	1667	2667	8	@70	100 household connection and stand posts. No pr filter. Only chlorination. OH tank
5	Santa-pada etc	Brahmani	8.88 Cr	18984	21807	39500	8	@100	WTP, UGR, ESR, Distribution system exists, Being augmented
6	Gurujang etc	Brahmani	4.84 Cr	6320	7260	13150	8	@100	WTP, UGR, ESR, Distribution system exists, Being augmented
			17Cr	30989	41072	72225			

Among the 6 sub-packages, sl no. 5 (i.e. Santapada etc) and sl no.6 (i.e. Gurujang etc) are major packages. Although MCL has released the first instalment of 15% against these packages, work has not yet started. Tender is under finalisation.

For package 1 to 4, MCL has disbursed 65% fund till August 2019.

The proposed infrastructure is as under:

Santapada etc:



Gurujang etc:

